


# John R Road Reconstruction

## Sequence of Construction Activity

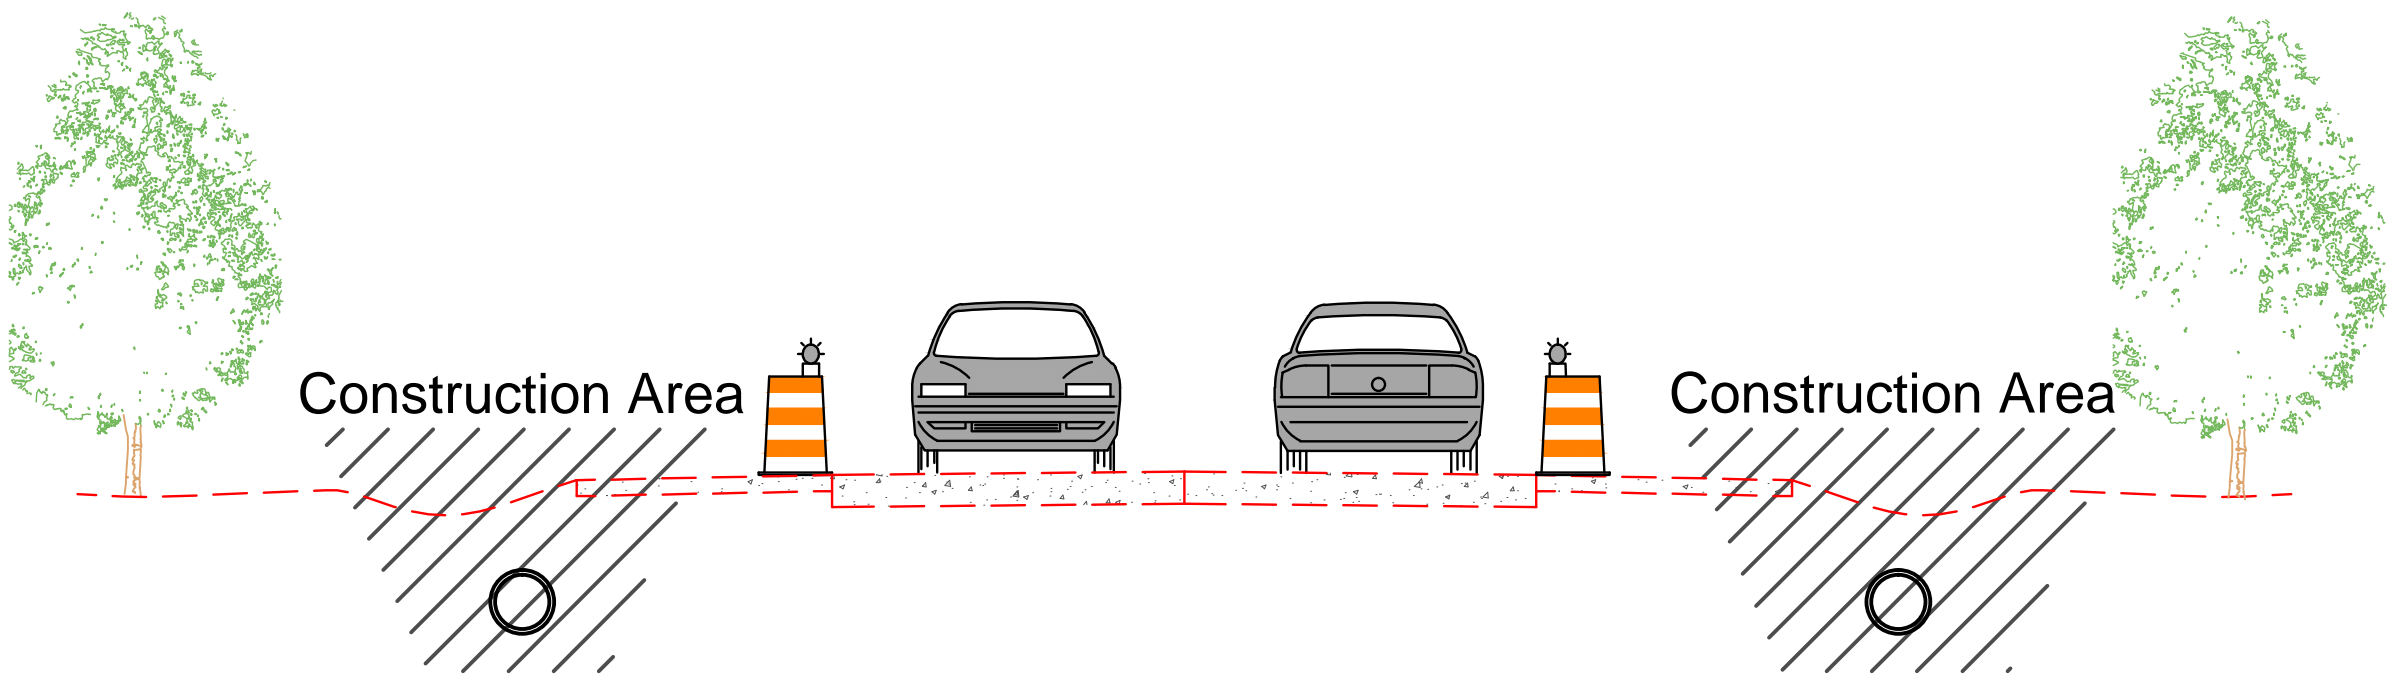


### Stage 1

Utility Construction

2-Way Traffic in Existing Lanes

October 2017 - March 2018

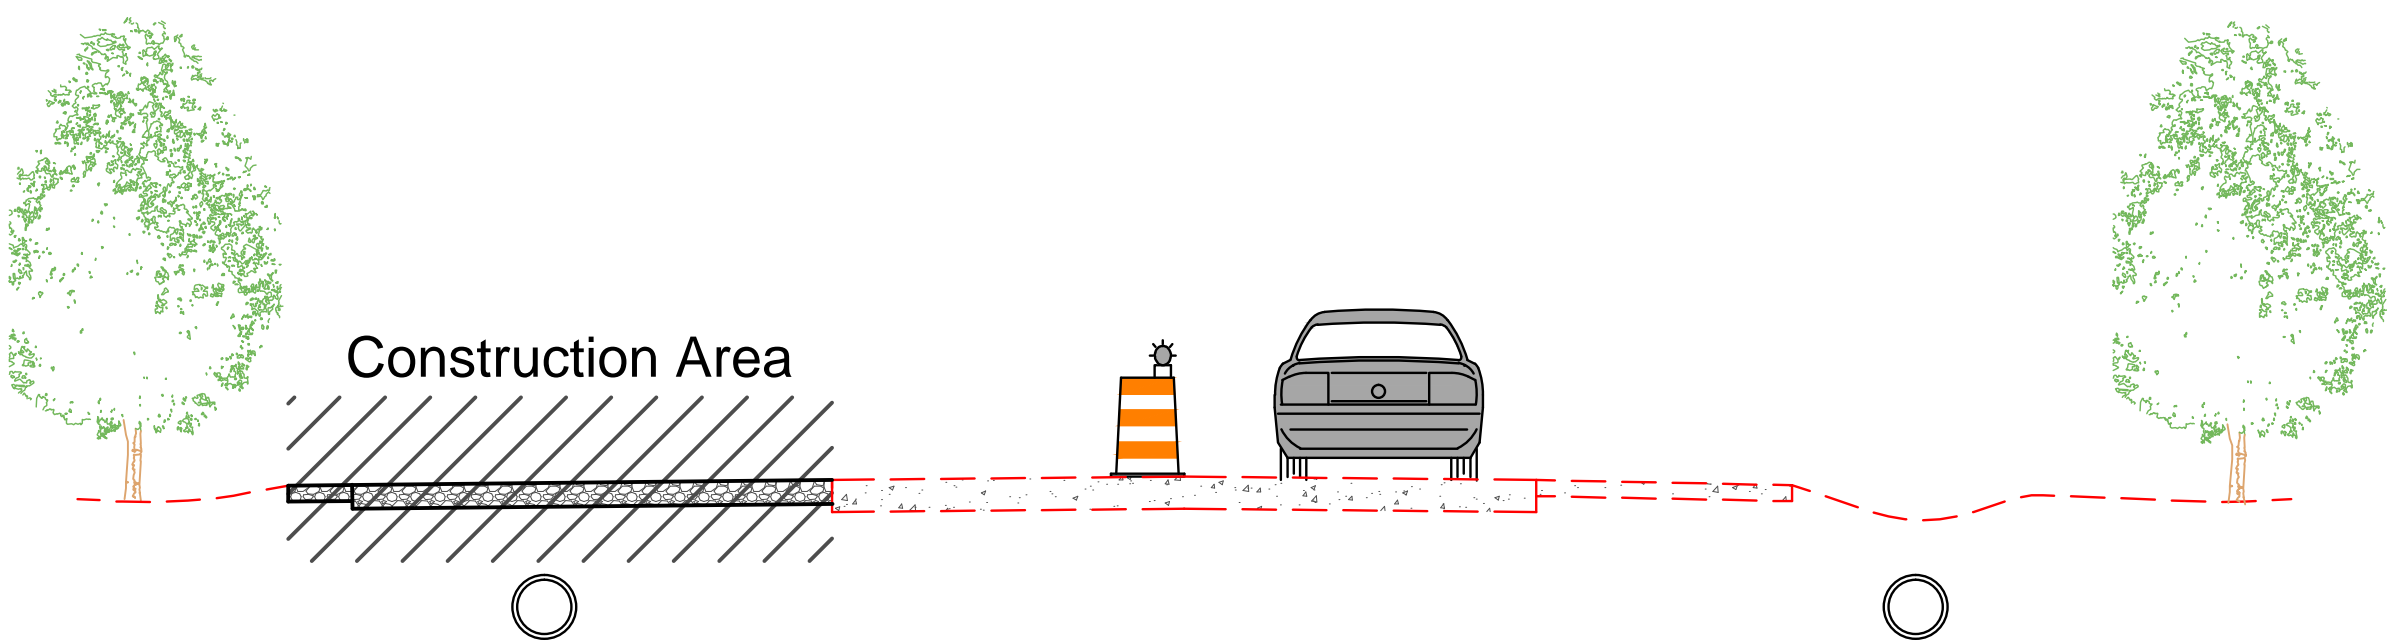


### Stage 2A

Temporary Pavement Construction

One Way Northbound Traffic in Existing Lane

April 2018

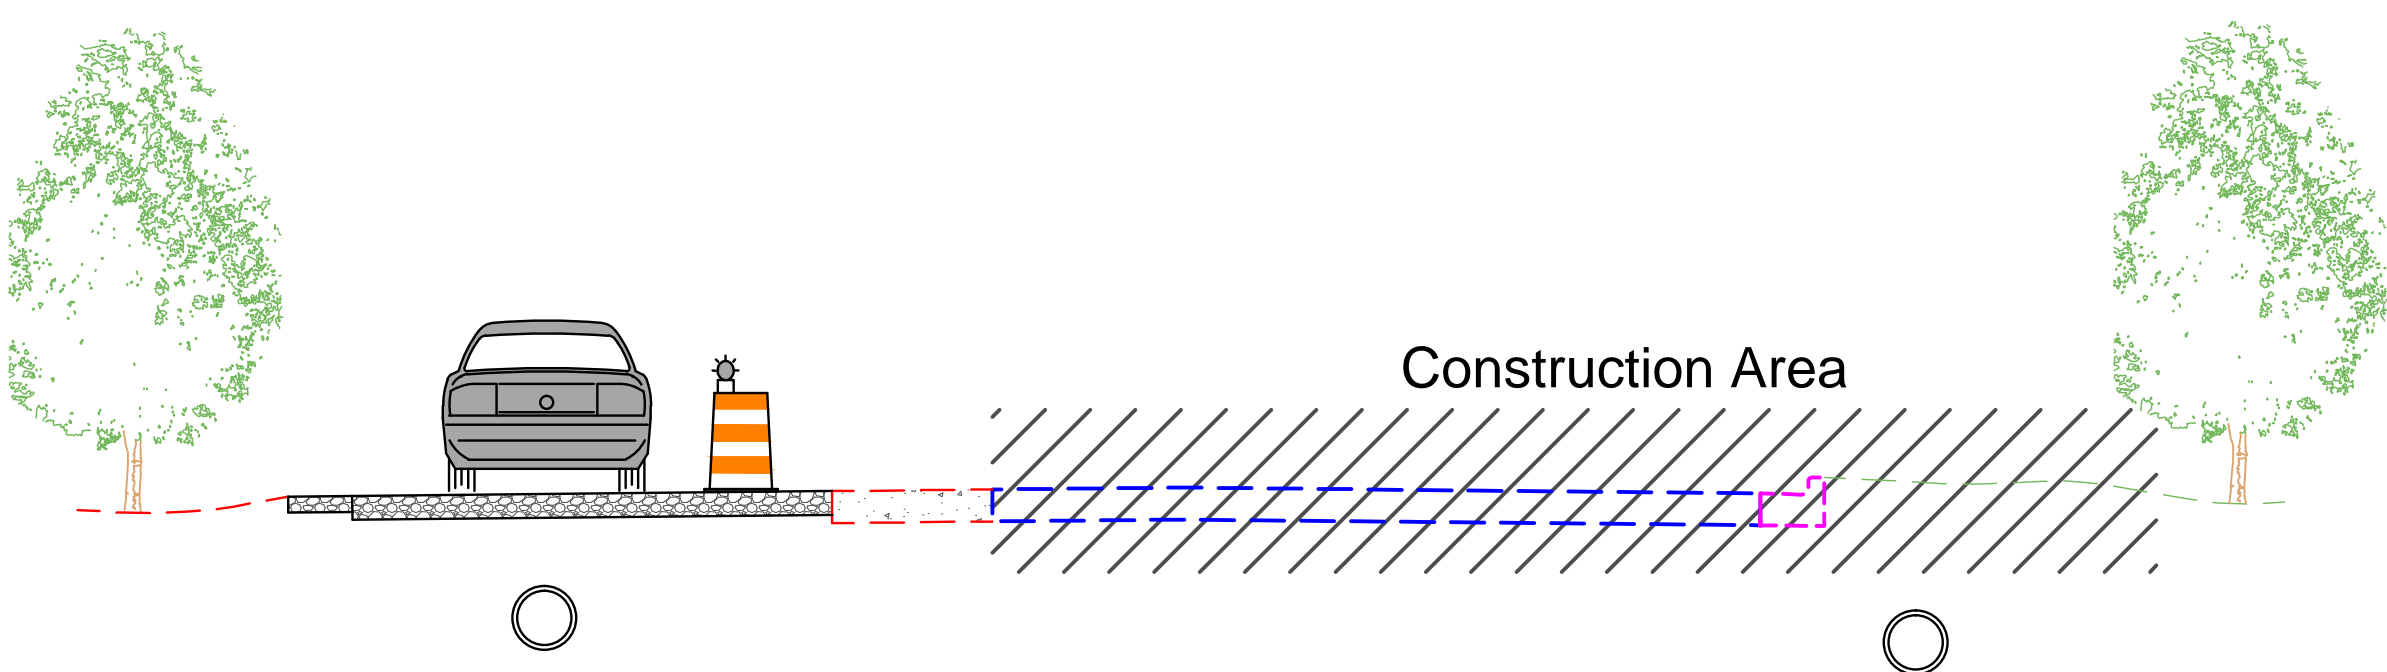


### Stage 2B

Northbound and Center Lane Construction

One Way Northbound Traffic on Temporary Pavement

April - July 2018

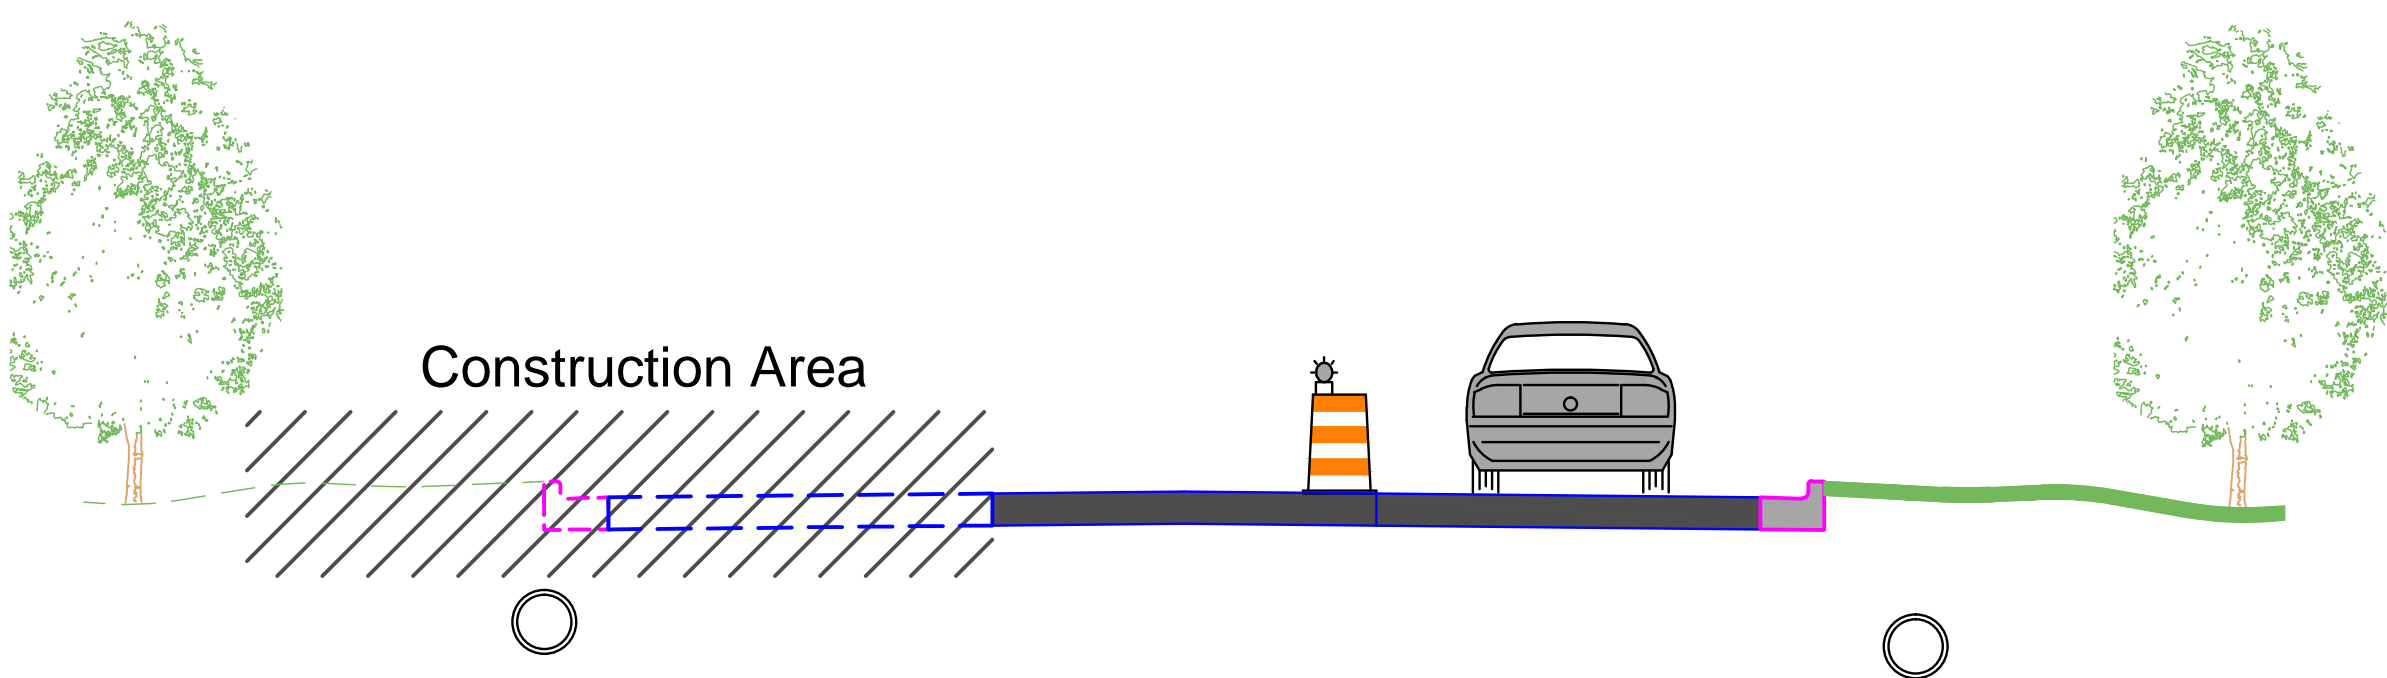


### Stage 3

Southbound Lane Construction

One Way Northbound Traffic on New Pavement

July - November 2018

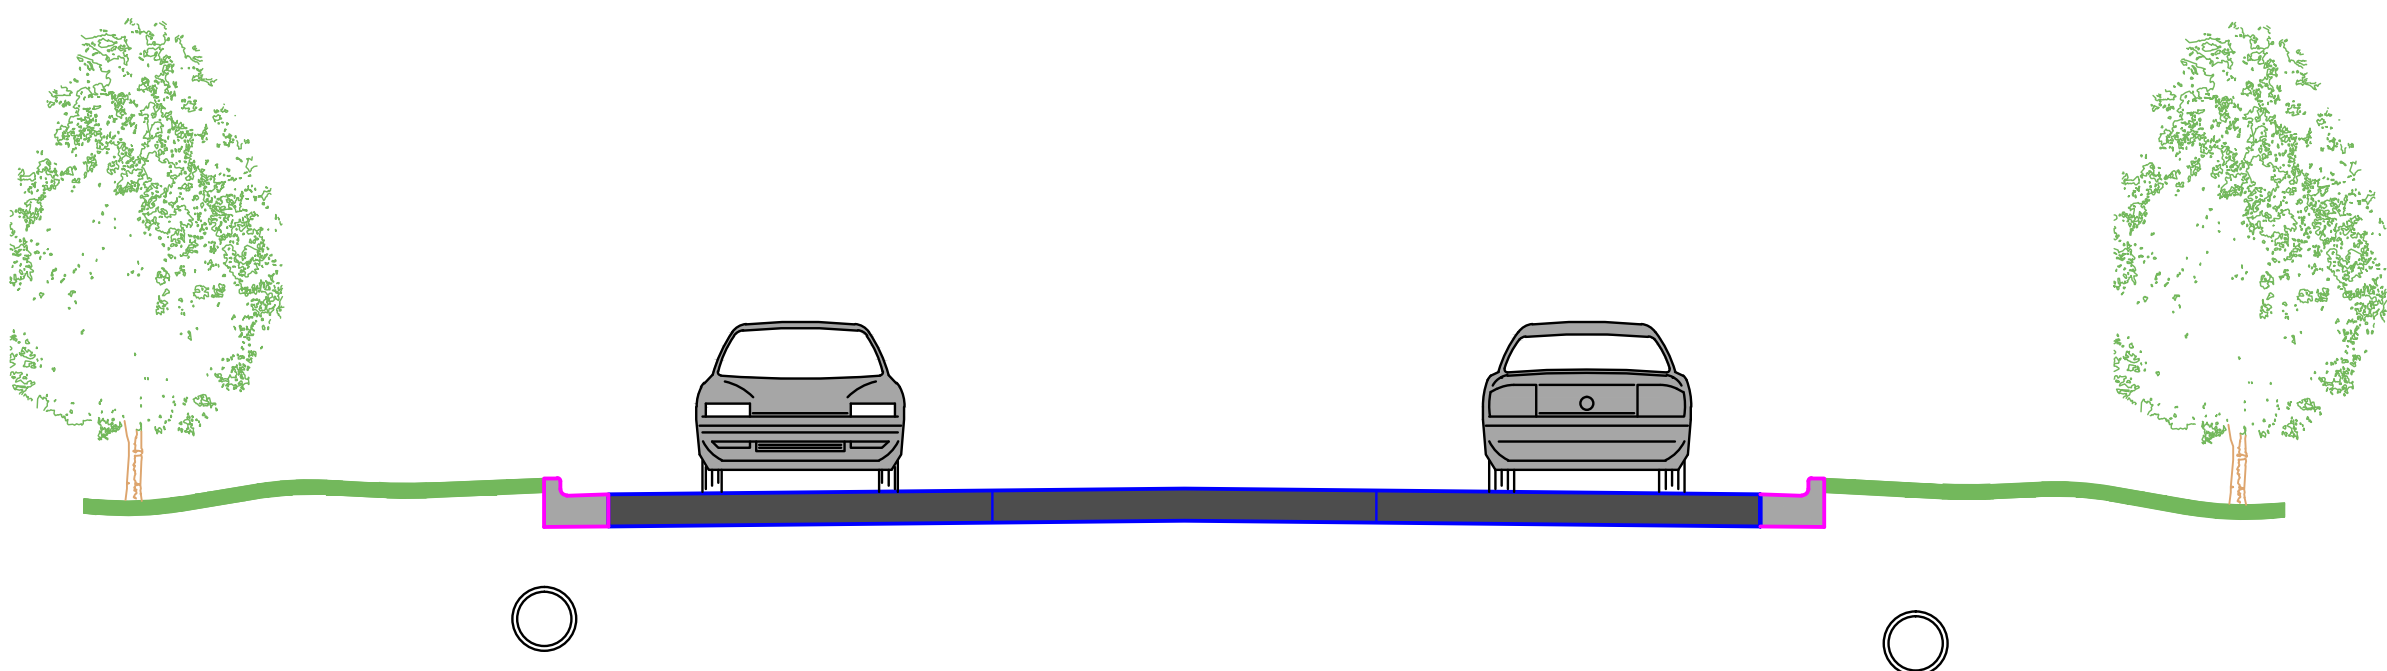

### Completed Project

Reconstructed Three Lane Roadway

November 2018
