## **Anticipated Construction Schedule**

Winter	October 2017 - Construction Begins
2017 Phase 1	October 2017 to March 2018 – Underground utility work including water main, sanitary sewer and storm sewer. Two-way traffic on John R Road with work outside of roadway.
	**Short term traffic interruptions are anticipated to install periodic utility crossings of the roadway**
Spring 2018	April 2018 to July 2018 – Construct temporary pavement, then build the northbound and center lanes of John R Road including
Phase 2	catch basins, pavement, driveways and side street approaches.  Traffic detour goes into effect. Northbound traffic only on John  R Road while southbound traffic is detoured.
Summer/	July 2018 to October 2018 – Construct the southbound lane of
Fall	John R Road including catch basins, pavement, driveways and side street approaches. <b>Northbound traffic only, southbound</b>
2018	traffic is detoured.
Phase 3	October 2018 to November 2018 – Open road to two-way traffic, complete pavement markings, signing and restoration work.
Expected Project Completion:	

NOVEMBER, 2018

### For additional information, contact:


City of Troy - Engineering Department Mr. William J. Huotari, P.E. Deputy City Engineer 500 W. Big Beaver Road Troy, MI 48084 (248) 524-3387 HuotariWJ@ troymi.gov





# **WELCOME**

**PUBLIC MEETING** December 8, 2015 John R Road Reconstruction Long Lake Road to South Boulevard

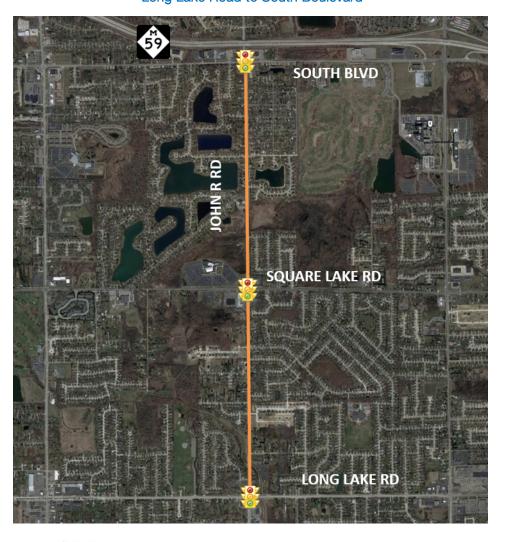





# John R Reconstruction Project

The John R Reconstruction project limits extend from the north side of the Long Lake Road intersection to the M-59 bridge over John R Road just north of South Boulevard. All side street approaches within these limits will be included in the reconstruction. The estimated construction cost (using combined federal and city funding) is \$14.7 million.

#### PROJECT INCLUDES:


- 2 miles of asphalt reconstruction
- 3 lanes wide with a continuous center left turn lane
- Curb and gutter and catch basins
- Addition of a continuous eight-foot wide sidewalk (east side)
- Addition of a continuous ten-foot wide asphalt path (west side)
- New water main and hydrants (Long Lake to Square Lake)
- Sanitary sewer construction (locations vary)
- Storm sewer construction
- Driveway replacements
- Two new traffic signals at Square Lake & South Blvd
- ► Sidewalk ramp replacement to meet current standards
- Bridge deck replacement at the Nelson Drain
- New signing and pavement markings
- New street lighting



You may have noticed work along John R Road earlier this year. Utility relocations are underway so utility work can be completed before roadway work begins.

#### **DETOUR**

▶ John R Road will remain open to normal two-way traffic during the first stage of the construction. Work will be completed to install new underground utility lines on each side of John R Road.

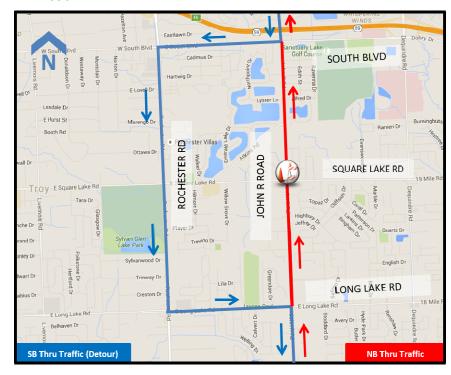

During the 2018 construction season John R Road will be closed to southbound traffic and will carry one-way traffic northbound. Southbound traffic will be detoured to Rochester Road.

### **KEY NOTES:**

- Access to businesses and residences will be maintained throughout the project
- Traffic through major cross roads will be maintained throughout the project
- ► Non-consecutive side street approaches may be closed for short durations, when neighborhoods have alternate access
